


THERMAL FIELD LOG

Project _____

Date Placed: _____

Pier No. _____

Shaft No. _____

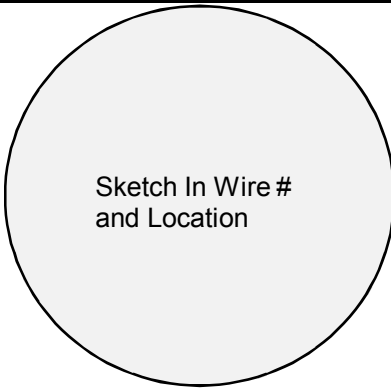


Wire #	Serial #	Wire Length (#nodes)	Nodes Above Concrete	Wire Tested After Install
1				
2				
3				
4				
5				
6				

Designate Northerly wire as #1

Wire-Wire Distance		
1-4 _____ in.	3-1 _____ in.	5-4 _____ in.
2-1 _____ in.	3-4 _____ in.	6-1 _____ in.
2-4 _____ in.	5-1 _____ in.	6-4 _____ in.

Shaft Information		
	Design	As-Built
Shaft Dia.	_____ in.	_____ in.
Shaft Length	_____ ft.	_____ ft.
Concrete Vol.	_____ cy.	_____ cy.
Cage Length	_____ ft.	_____ ft.
Cage Dia.	_____ in.	_____ in.
Casing Dia. (perm./temp.)	_____ in.	_____ in.
Casing Length	_____ ft.	_____ ft.
Rock Socket Dia.	_____ in.	_____ in.
Rock Socket Length	_____ ft.	_____ ft.

Elevation

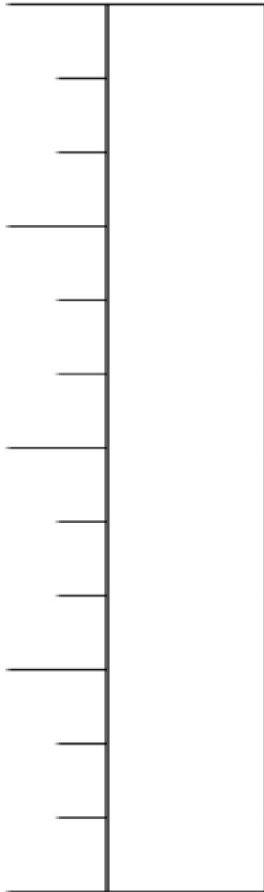

* indicate changes in diameter

Field Notes:

Start of Placement -
End of Placement -
Placement Method -

Legend

- TOC Top of Casing
- TOG Top of Ground
- TOS Top of Shaft
- TORS Top of Rock Socket
- BOC Bottom of Casing
- BORC Bottom of Reinf. Cage
- BOS Bottom of Shaft
- ▼ Water Level

Completed By: _____

Please Submit with Concrete
 Placement Log and Installation Record

6 Wire - Shaft
