


THERMAL FIELD LOG

Project _____

Date Placed: _____

Pier No. _____

Shaft No. _____

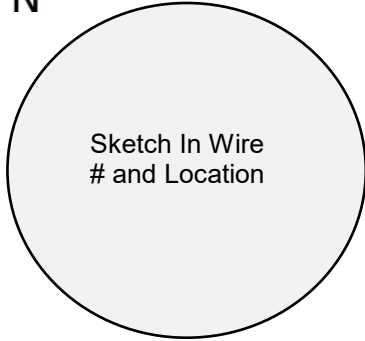


Wire #	Wire Serial #	Wire Suffix	Wire Length (#nodes)	Nodes Above Concrete	Splice 1		Splice 2		Tested After Install
					Offset	Overlap	Offset	Overlap	
1									
2									
3									
4									
5									
6									
7									
8									
9									

Designate Northerly wire as #1

Wire-Wire Distance

1-5 ___ cm. 4-1 ___ cm. 7-5 ___ cm.
 2-1 ___ cm. 4-5 ___ cm. 8-1 ___ cm.
 2-5 ___ cm. 6-1 ___ cm. 8-5 ___ cm.
 3-1 ___ cm. 6-5 ___ cm. 9-1 ___ cm.
 3-5 ___ cm. 7-1 ___ cm. 9-6 ___ cm.

Elevation

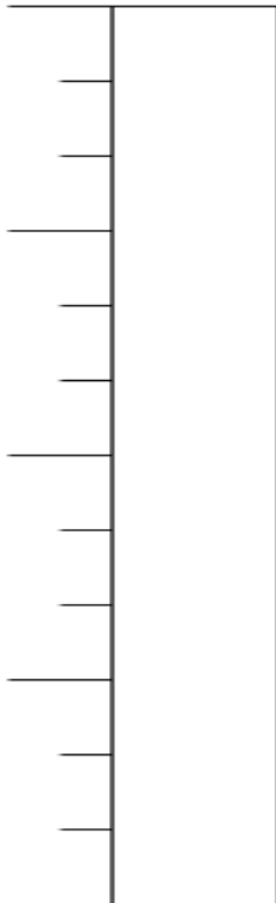

* indicate changes in diameter

Shaft Information

	Design	As-Built
Shaft Dia.	_____ cm.	_____ cm.
Shaft Length	_____ m.	_____ m.
Concrete Vol.	_____ cbm.	_____ cbm.
Cage Length	_____ m.	_____ m.
Cage Dia.	_____ cm.	_____ cm.
Casing Dia. (perm./temp.)	_____ cm.	_____ cm.
Casing Length	_____ m.	_____ m.
Rock Socket Dia.	_____ cm.	_____ cm.
Rock Socket Length	_____ m.	_____ m.
Distance Between Bottom of Cage and Bottom Node	_____ cm.	_____ cm.

Field Notes:

Start of Placement -
 End of Placement -
 Placement Method -

Legend

TOC	Top of Casing	BOC	Bottom of Casing
TOG	Top of Ground	BORC	Bottom of Reinf. Cage
TOS	Top of Shaft	BOS	Bottom of Shaft
TORS	Top of Rock Socket		Water Level

Completed By: _____

Submit with Concrete Placement
 Log and Installation Record

9 Wire - Shaft
