


# THERMAL FIELD LOG

Project \_\_\_\_\_  
 Pier No. \_\_\_\_\_

Date Placed: \_\_\_\_\_  
 Shaft No. \_\_\_\_\_

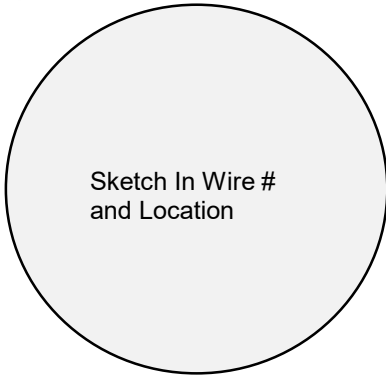

Wire #	Wire Serial #	Wire Suffix	Data Logger Serial #	Wire Length (#nodes)	Nodes Above Concrete	Wire Tested
1						
2						

Designate Northerly wire as #1

Wire-Wire Distance
1-2 _____ in.

Shaft Information	
	<b>As-Built</b>
Shaft Dia.	_____ in.
Shaft Length	_____ ft.
Concrete Vol.	_____ cy.
Cage Length	_____ ft.
Cage Dia.	_____ in.
Casing Dia. Circle: (perm./temp.)	_____ in.
Casing Length	_____ ft.
Rock Socket Dia.	_____ in.
Rock Socket Length	_____ ft.
Distance Between TOS & Top of Cage	_____ in.
Distance Between BOS & Bottom Node	_____ in.


**\*\*When Cage is suspended, bottom node should be 1/2in from bottom of cage. When cage isn't suspended, bottom node should be placed 2in from bottom of cage\*\***

**Field Notes:**  
 Start of Placement - \_\_\_\_\_  
 End of Placement - \_\_\_\_\_  
 Placement Method (Tremie Pipe or Free Fall)- \_\_\_\_\_

Legend			
TOC	Top of Casing	BOC	Bottom of Casing
TOG	Top of Ground	BORC	Bottom of Reinf. Cage
TOS	Top of Shaft	BOS	Bottom of Shaft
TORS	Top of Rock Socket	▼	Water Level

--

Elevation

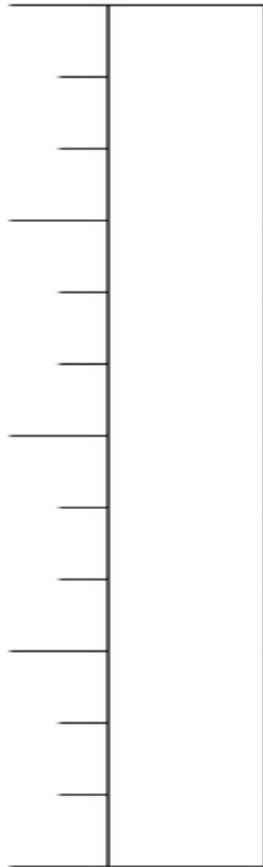

\* indicate changes in diameter

Completed By: \_\_\_\_\_

Submit with Concrete Placement  
 Log and Installation Record

2 Wire - Shaft
